


# Construction Schedule: Mack Point Phase 1

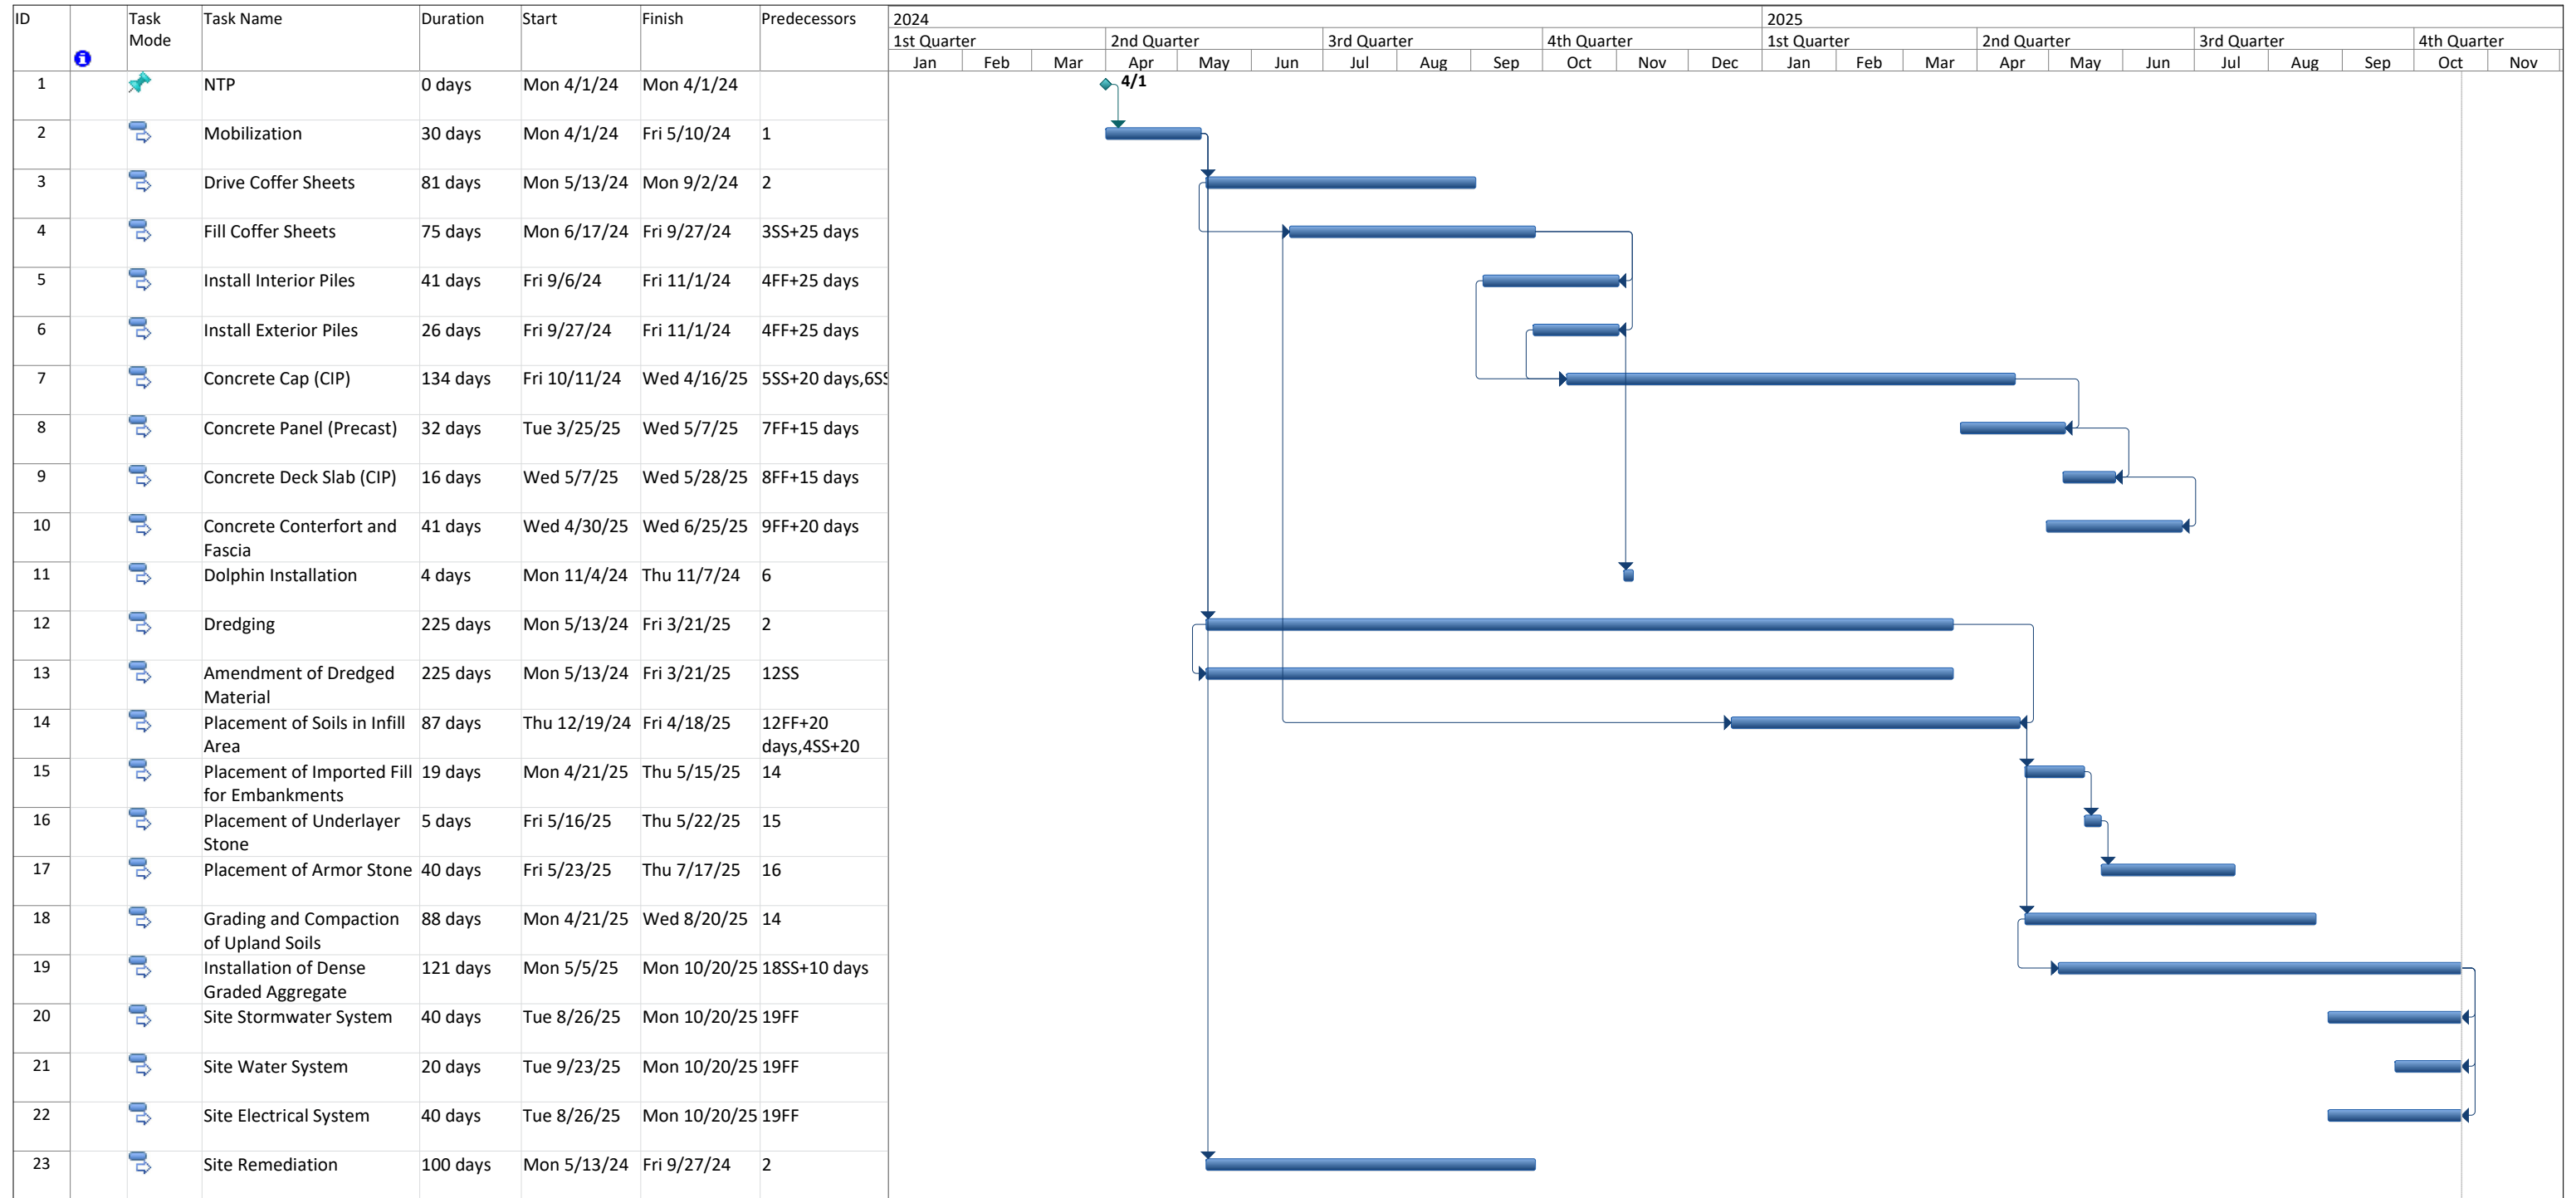

Mack Point Phase 1  
11/17/21

	Task		Summary		External Milestone		Inactive Summary		Manual Summary Rollup		Finish-only
	Split		Project Summary		Inactive Task		Manual Task		Manual Summary		Deadline
	Milestone		External Tasks		Inactive Milestone		Duration-only		Start-only		Progress

## Construction Schedule: Mack Point Phase 2

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	2024												2025												2026											
							1st Quarter			2nd Quarter			3rd Quarter			4th Quarter			1st Quarter			2nd Quarter			3rd Quarter			4th Quarter			1st Quarter			2nd Quarter			3rd Quarter			4th Quarter		
							Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	Dec	Jan	Feb	Mar	Apr	May	Jun	Jul	Aug	Sep	Oct	Nov	
1		NTP	0 days	Mon 4/1/24	Mon 4/1/24		4/1																																			
2		Mobilization	30 days	Mon 4/1/24	Fri 5/10/24	1	[Gantt bar: Mon 4/1/24 to Fri 5/10/24]																																			
3		Drive Coffer Sheets	201 days	Mon 5/13/24	Mon 2/17/25	2	[Gantt bar: Mon 5/13/24 to Mon 2/17/25]																																			
4		Fill Coffer Sheets	203 days	Mon 6/17/24	Wed 3/26/25	3SS+25 days	[Gantt bar: Mon 6/17/24 to Wed 3/26/25]																																			
5		Install Interior Piles	98 days	Mon 12/16/24	Wed 4/30/25	4FF+25 days	[Gantt bar: Mon 12/16/24 to Wed 4/30/25]																																			
6		Install Exterior Piles	64 days	Fri 1/31/25	Wed 4/30/25	4FF+25 days	[Gantt bar: Fri 1/31/25 to Wed 4/30/25]																																			
7		Concrete Cap (CIP)	322 days	Fri 2/14/25	Mon 5/11/26	5SS+20 days, 6SS	[Gantt bar: Fri 2/14/25 to Mon 5/11/26]																																			
8		Concrete Panel (Precast)	78 days	Thu 3/5/26	Mon 6/22/26	7FF+30 days	[Gantt bar: Thu 3/5/26 to Mon 6/22/26]																																			
9		Concrete Deck Slab (CIP)	39 days	Wed 5/20/26	Mon 7/13/26	8FF+15 days	[Gantt bar: Wed 5/20/26 to Mon 7/13/26]																																			
10		Concrete Conterfort and Fascia	101 days	Mon 3/23/26	Mon 8/10/26	9FF+20 days	[Gantt bar: Mon 3/23/26 to Mon 8/10/26]																																			
11		Dredging	300 days	Mon 5/13/24	Fri 7/4/25	2	[Gantt bar: Mon 5/13/24 to Fri 7/4/25]																																			
12		Amendment of Dredged Material	300 days	Mon 5/13/24	Fri 7/4/25	11SS	[Gantt bar: Mon 5/13/24 to Fri 7/4/25]																																			
13		Placement of Dredged Soils in Infill Area	233 days	Wed 9/11/24	Fri 8/1/25	11FF+20 days, 4SS+20	[Gantt bar: Wed 9/11/24 to Fri 8/1/25]																																			
14		Placement of Imported Fill for Infill	35 days	Mon 8/4/25	Fri 9/19/25	13	[Gantt bar: Mon 8/4/25 to Fri 9/19/25]																																			
15		Placement of Imported Fill for Embankments	19 days	Mon 9/22/25	Thu 10/16/25	14	[Gantt bar: Mon 9/22/25 to Thu 10/16/25]																																			
16		Underlayer Stone Placement	5 days	Fri 10/17/25	Thu 10/23/25	15	[Gantt bar: Fri 10/17/25 to Thu 10/23/25]																																			
17		Armor Stone Placement	40 days	Fri 10/24/25	Thu 12/18/25	16	[Gantt bar: Fri 10/24/25 to Thu 12/18/25]																																			
18		Grading and Compaction of Upland Soils	116 days	Mon 9/22/25	Mon 3/2/26	14	[Gantt bar: Mon 9/22/25 to Mon 3/2/26]																																			
19		Installation of Dense Graded Aggregate	202 days	Mon 10/6/25	Tue 7/14/26	18SS+10 days	[Gantt bar: Mon 10/6/25 to Tue 7/14/26]																																			
20		Site Stormwater System	40 days	Wed 5/20/26	Tue 7/14/26	19FF	[Gantt bar: Wed 5/20/26 to Tue 7/14/26]																																			
21		Site Water System	20 days	Wed 6/17/26	Tue 7/14/26	19FF	[Gantt bar: Wed 6/17/26 to Tue 7/14/26]																																			
22		Site Electrical System	40 days	Wed 5/20/26	Tue 7/14/26	19FF	[Gantt bar: Wed 5/20/26 to Tue 7/14/26]																																			
23		Site Remediation	100 days	Mon 5/13/24	Fri 9/27/24	2	[Gantt bar: Mon 5/13/24 to Fri 9/27/24]																																			

Mack Point Phase 2 11/17/21	Task		Summary		External Milestone		Inactive Summary		Manual Task		Manual Summary		Finish-only	
	Split		Project Summary		Inactive Task			Duration-only			Manual Summary Rollup		Deadline	
	Milestone		External Tasks		Inactive Milestone				Start-only			Progress		



## Construction Schedule: Sears Island Phase 2

ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	Resource Names	2024				2025				2026				2027				2028		
								Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3	Qtr 4	Qtr 1	Qtr 2	Qtr 3
1		NTP	0 days	Mon 4/1/24	Mon 4/1/24																					
2		Mobilization	30 days	Mon 4/1/24	Fri 5/10/24	1																				
3		Drive Coffe Sheets	201 days	Mon 5/13/24	Mon 2/17/25	2																				
4		Fill Coffe Sheets	203 days	Mon 6/17/24	Wed 3/26/25	3SS+25 days																				
5		Install Interior Piles	98 days	Mon 7/22/24	Wed 12/4/24	4SS+25 days																				
6		Install Exterior Piles	64 days	Mon 7/22/24	Thu 10/17/24	4SS+25 days																				
7		Concrete Cap (CIP)	322 days	Mon 8/19/24	Tue 11/11/25	5SS+20 days,6SS																				
8		Concrete Panel (Precast)	78 days	Fri 8/22/25	Tue 12/9/25	7FF+20 days																				
9		Concrete Deck Slab (CIP)	39 days	Thu 11/6/25	Tue 12/30/25	8FF+15 days																				
10		Concrete Conterfort and Fascia	101 days	Tue 9/9/25	Tue 1/27/26	9FF+20 days																				
11		Soil Cut from Uplands	338 days	Mon 7/15/24	Wed 10/29/25	2,4SS+20 days																				
12		Placement of Soils in Infill Area	233 days	Mon 8/12/24	Wed 7/2/25	11SS+20 days,4SS+20																				
13		Underlayer Stone Placement	5 days	Thu 7/3/25	Wed 7/9/25	12																				
14		Armor Stone Placement	45 days	Thu 7/10/25	Wed 9/10/25	13																				
15		Placement of Soil Surcharge	201 days	Thu 7/3/25	Thu 4/9/26	11FF+5 days,12																				
16		Surcharge Duration	135 days	Fri 4/10/26	Thu 10/15/26	15																				
17		Removal of Soil Surcharge	181 days	Fri 10/16/26	Fri 6/25/27	16																				
18		Grading and Compaction of Upland Soils	127 days	Mon 6/28/27	Tue 12/21/27	17																				
19		Installation of Dense Graded Aggregate	203 days	Mon 7/12/27	Wed 4/19/28	18SS+10 days																				
20		Site Stormwater System	40 days	Thu 2/24/28	Wed 4/19/28	19FF																				
21		Site Water System	20 days	Thu 3/23/28	Wed 4/19/28	19FF																				
22		Site Electrical System	40 days	Thu 2/24/28	Wed 4/19/28	19FF																				
23		Utilities onto Island	500 days	Mon 5/13/24	Fri 4/10/26	2																				
24		Site Remediation	100 days	Mon 5/13/24	Fri 9/27/24	2																				

Sears Island Phase 2  
11/17/21

Task		Summary		External Milestone		Inactive Summary		Manual Task		Manual Summary		Deadline	
Split		Project Summary		Inactive Task		Manual Summary Rollup		Manual Summary		Manual Summary		Deadline	
Milestone		External Tasks		Inactive Milestone		Duration-only		Start-only		Start-only		Progress	
